





Post-Construction Haul Route Evaluation (2020)

Work Orders in Hyde County, SD
Triple H Wind Farm

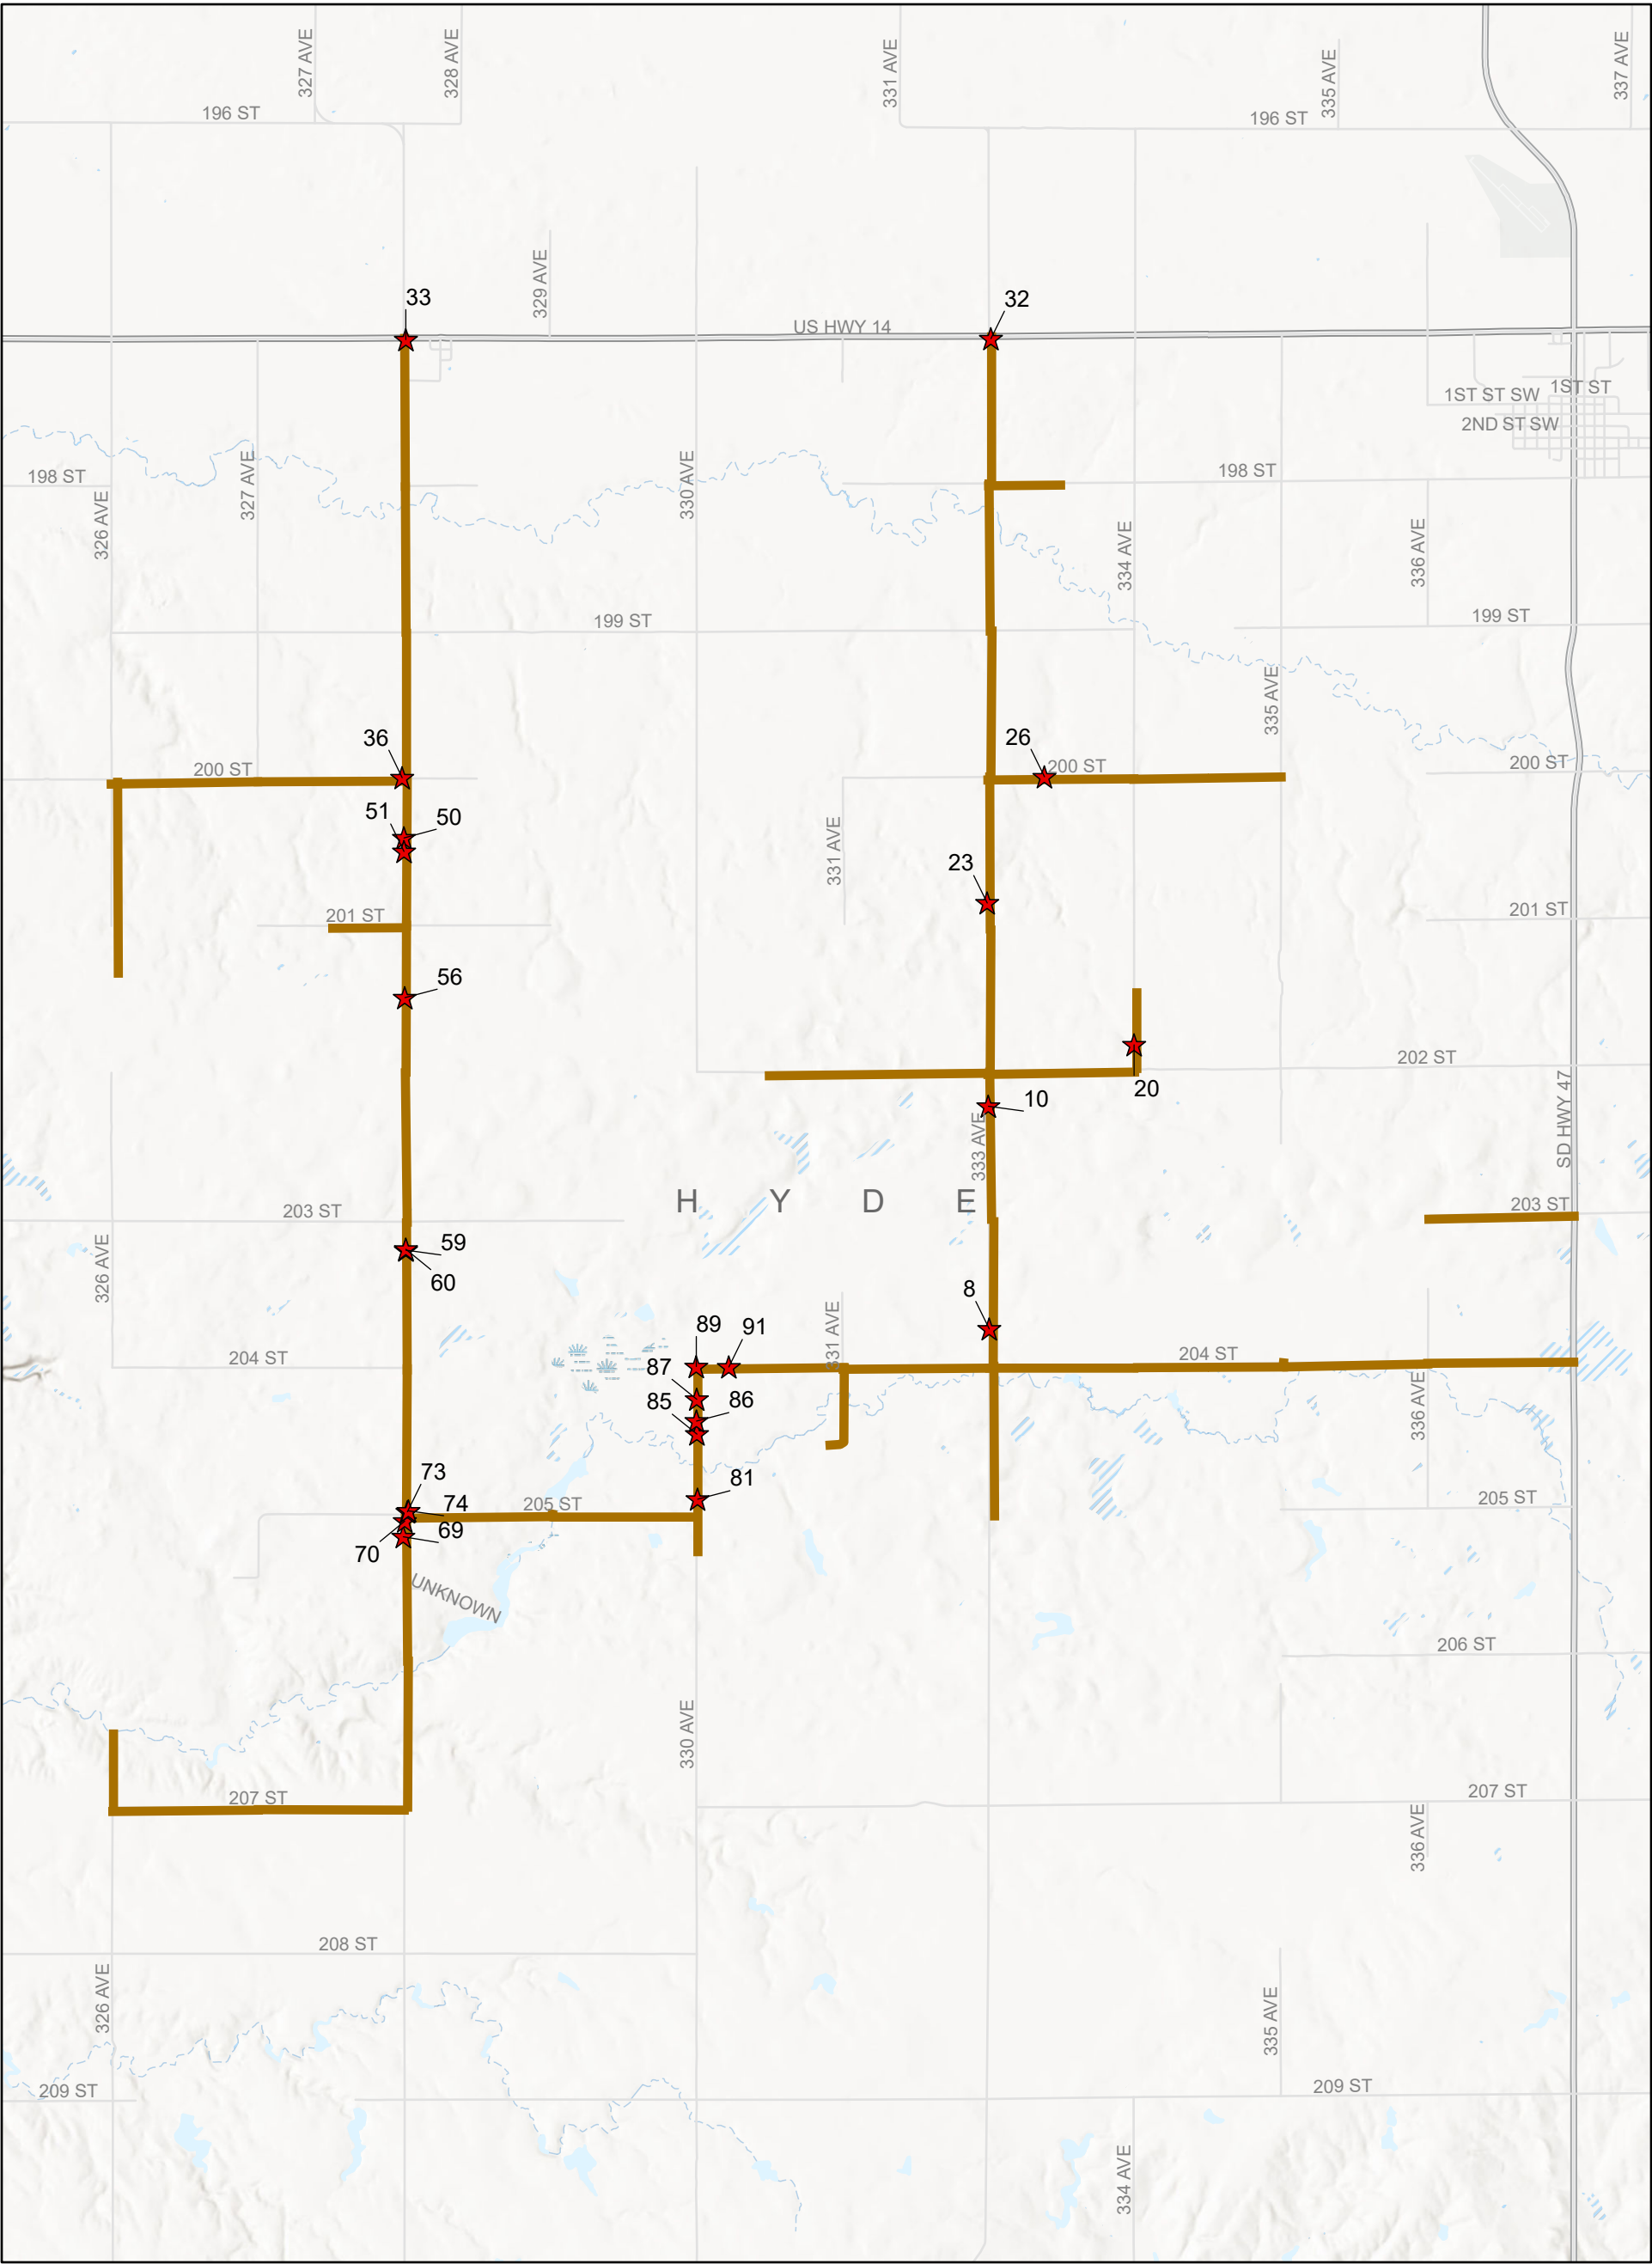


We listen. We solve.®



Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 8

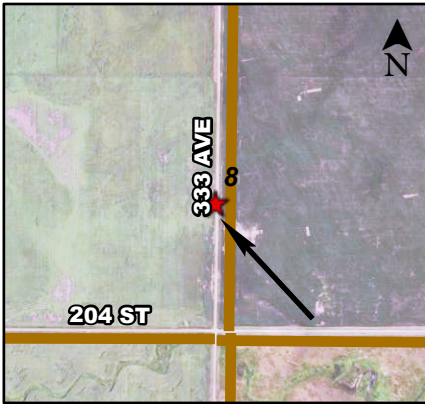


ID	8	Owner	Hyde County
Route	333 Ave	Location	0.25 mi North of 204 St
Contractor Direction			
Regrade rutting to match existing inslope/drainage. West side of road.			



Smooth out ruts so ditch can be mowed.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 10

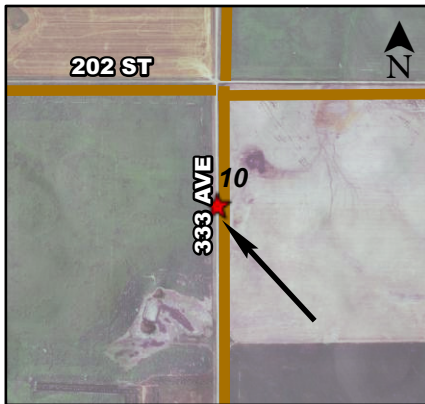


ID	10	Owner	Hyde County
Route	333 Ave	Location	0.25 mi South of 202 St
Contractor Direction			
Regrade rutting to match existing inslope/drainage. East side of road.			



Smooth out ruts so ditch can be mowed.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 20

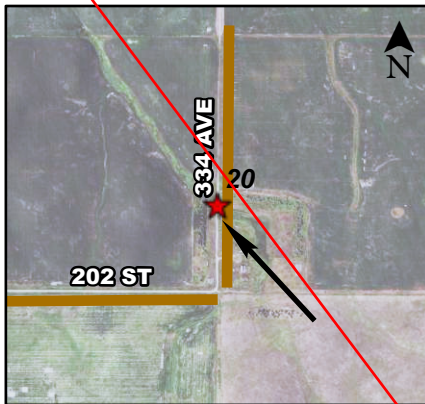

ID	20	Owner	Hyde County
Route	334 Ave	Location	0.15 mi North of 202 St
Contractor Direction			
Clean out culvert pipe on both sides.			




OK, Roberts, and Stangohr



We listen. We solve.®

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 23

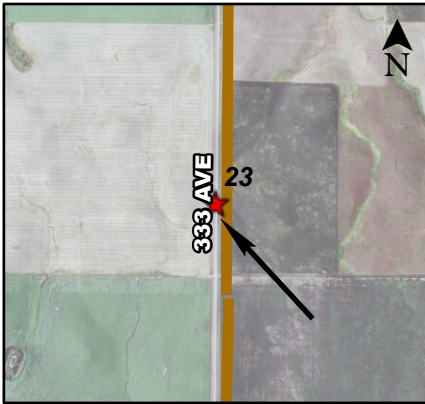


ID	23	Owner	Hyde County
Route	333 Ave	Location	0.85 mi South of 200 St
Contractor Direction			
Repair both ends of culvert pipe on western approach to intersection.			



Straighten pipe end with handyman jack

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 26

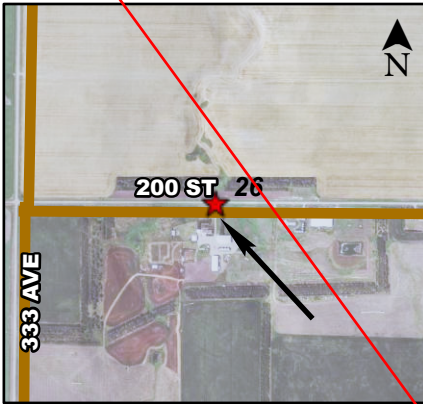


ID	26	Owner	Hyde County
Route	200 St	Location	0.4 mi East of 333 Ave
Contractor Direction			
Regrade/dirt/seed to match existing inslope/drainage. Both sides of road.			



OK Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 32

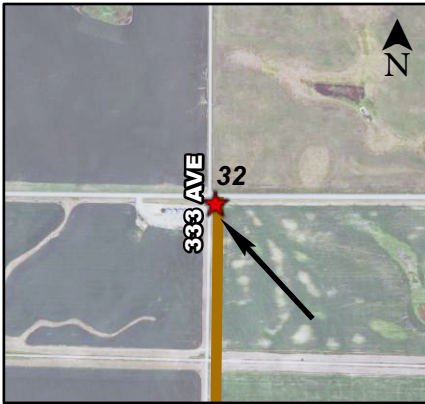


ID	32	Owner	Hyde County
Route	333 Ave	Location	At US 14
Contractor Direction			
Replace damaged R1-1 stop sign, post, and anchor and install per standard. Southeast corner.			



Need DOT breakaway and post.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 33

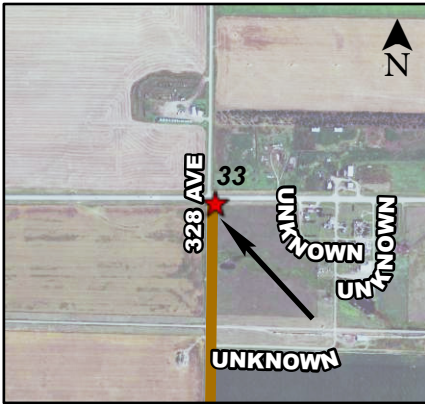


ID	33	Owner	Hyde County
Route	328 Ave	Location	At US 14
Contractor Direction			
Replace damaged R1-1 stop sign. Post okay. Southeast corner.			



Post is ok, needs new sign.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 36

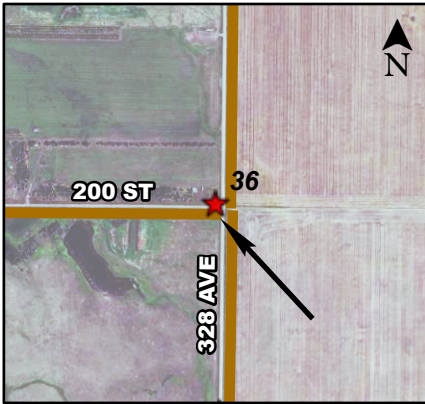


ID	36	Owner	Hyde County
Route	200 St	Location	0.01 mi West of 328 Ave
Contractor Direction			
Culvert pipe is completely buried on south end. Reestablish/Repair culvert and drainage.			



The pipe in this corner is smashed flat, replace 6' or so of the end.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 50

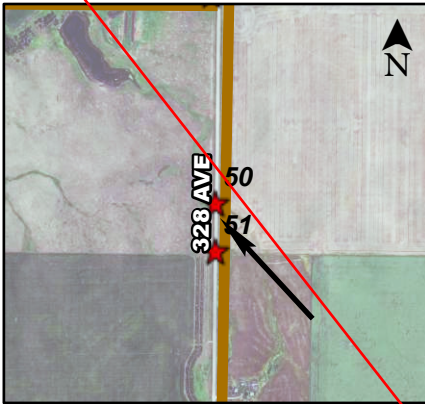


ID	50	Owner	Hyde County
Route	328 Ave	Location	0.4 mi South of 200 St
Contractor Direction			
Repair east end of culvert pipe. Replace object marker on east end.			



OK, Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 51

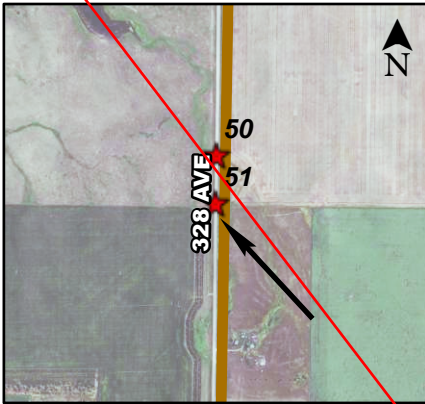


ID	51	Owner	Hyde County
Route	328 Ave	Location	0.5 mi South of 200 St
Contractor Direction			
Inslopes of approach on west side are too steep. Fill/regrade to flatten the inslopes of the approach.			



OK, Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 56

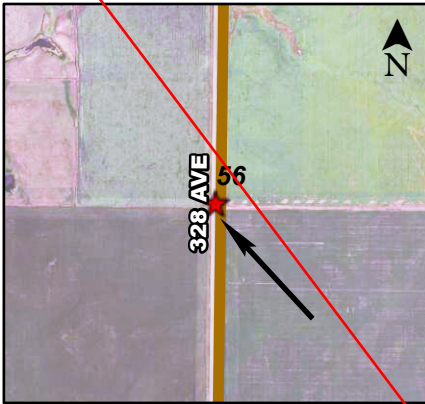


ID	56	Owner	Hyde County
Route	328 Ave	Location	0.5 mi South of 201 St
Contractor Direction			
Clean out culvert pipe.			



OK, Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 59

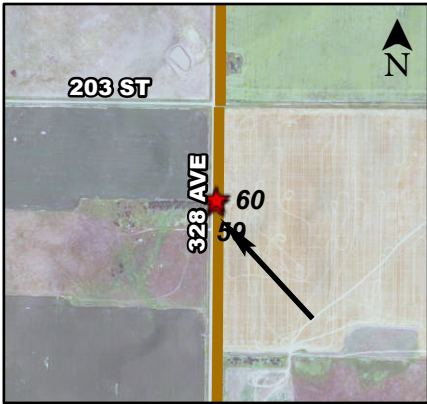

ID	59	Owner	Hyde County
Route	328 Ave	Location	0.2 mi South of 203 St
Contractor Direction			
Haul away large field stones from inslope/ditch.			



Remove Field Stones

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 60



ID	60	Owner	Hyde County
Route	328 Ave	Location	0.2 mi South of 203 St
Contractor Direction			
Clean out culvert pipe.			



OK, Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 69




ID	69	Owner	Hyde County
Route	328 Ave	Location	0.15 mi South of 205 St
Contractor Direction			
Clean out culvert pipe.			



OK, Roberts, and Stangohr

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 70

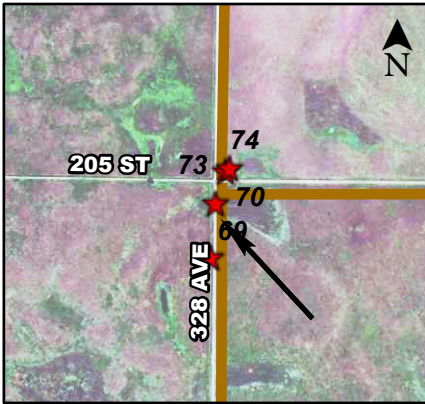

ID	70	Owner	Hyde County
Route	328 Ave	Location	0.05 mi South of 205 St
Contractor Direction			
Culvert pipe is completely buried on east end, partially on west end. Reestablish/Repair culvert and drainage.			




Contractor to expose East End



County will expose West End

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 73

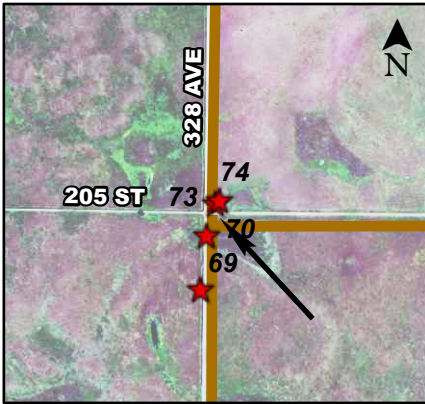


ID	73	Owner	Hyde County
Route	205 St	Location	At 328 St
Contractor Direction			
Replace damaged R1-1 stop sign and Del-8a tubular white delineator. Post okay. Northeast corner.			



Replace sign, post is ok.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 74

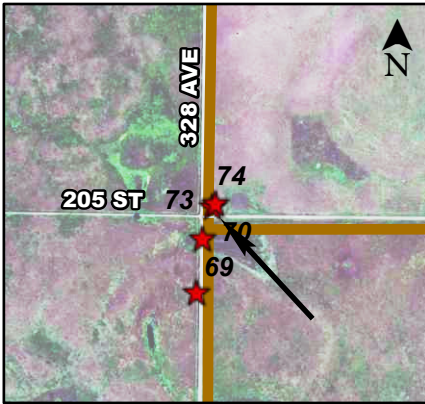


ID	74	Owner	Hyde County
Route	205 St	Location	At 328 St
Contractor Direction			
Replace damaged D3-1 street signs, post, and anchor and install per standard. Also replace missing D3-1 street signs.			



Replace

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 81

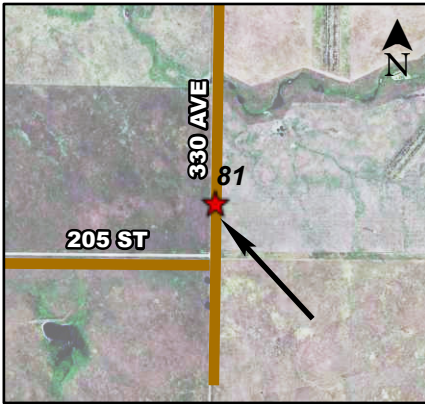


ID	81	Owner	Hyde County
Route	330 Ave	Location	0.1 mi North of 205 St
Contractor Direction			
Regrade rutting to match existing inslope/drainage. East side of road.			



Smooth ruts so ditch can be mowed.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 85

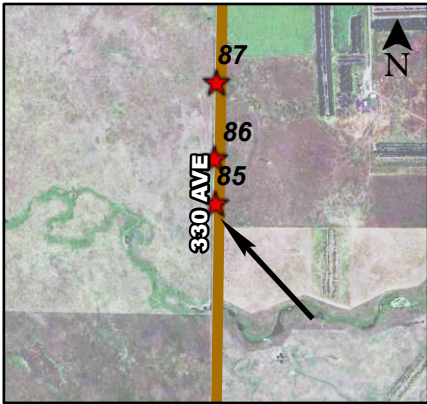


ID	85	Owner	Hyde County
Route	330 Ave	Location	0.45 mi South of 204 St
Contractor Direction			
Haul away large field stones from inslope/ditch.			



Remove Field Stones

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 86

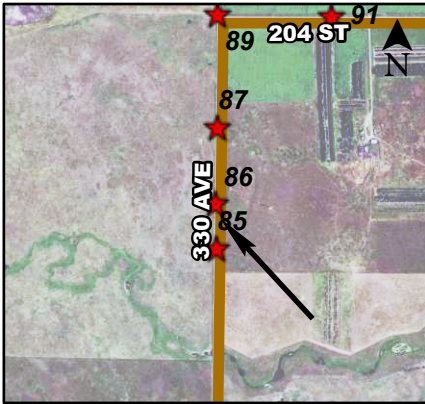

ID	86	Owner	Hyde County
Route	330 Ave	Location	0.35 mi South of 204 St
Contractor Direction			
Regrade rutting to match existing inslope/drainage. East side of road, approximately 100 feet long.			



Smooth ruts so ditch can be mowed.



Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 87




ID	87	Owner	Hyde County
Route	330 Ave	Location	0.2 mi South of 204 St
Contractor Direction			
Haul away gravel from inslope/ditch, regrade rutting to match existing inslope/drainage. East side of road.			



Smooth ruts so ditch can be mowed.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 89

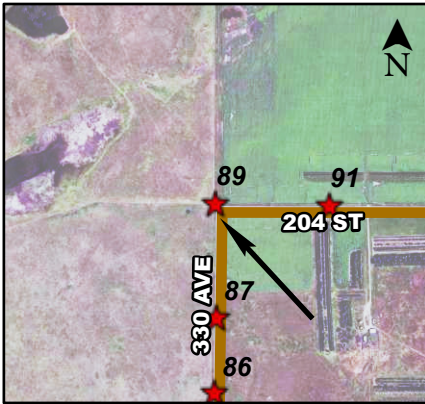


ID	89	Owner	Hyde County
Route	330 Ave	Location	At 204 St
Contractor Direction			
Replace damaged W1-8 chevron signs. Reset signs, posts, and anchor per standard if undamaged.			



Straighten posts and cheverons, they are not pointing correctly.

Post-Construction Haul Route Punch List 1

Triple H Wind Farm - Work Order ID # 91

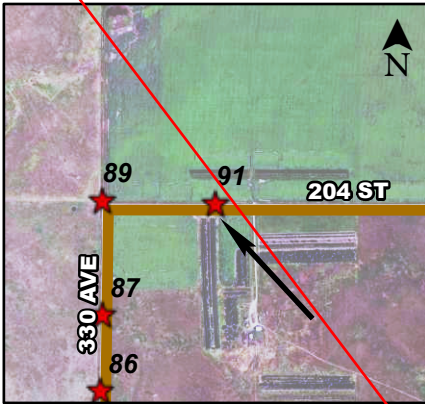

ID	91	Owner	Hyde County
Route	204 St	Location	0.2 mi East of 330 Ave
Contractor Direction			
Culvert pipe is overexposed. Fill/regrade the inslopes of turbine access on north side of road.			



OK, Roberts, and Stangohr
